

CITY OF SACRAMENTO
1231 I Street, Sacramento, CA 95814

Permit No: 0406506
Insp Area: 4
Thos Bros: 257C5

Site Address: 1807 SPALETTA WY SAC
Parcel No: 201-0940-091 REGENCY PARK B LOT 91

Sub-Type: NSFR
Housing (Y/N): N

CONTRACTOR
PULTE HOME CORP.
985 SUN CITY LN.
LINCOLN CA. 95648

OWNER

ARCHITECT

Nature of Work: MP1871 2 STORY 7 ROOM SFR

CONSTRUCTION LENDING AGENCY : I hereby affirm under penalty of perjury that there is a construction lending agency for the performance of the work for which this permit is issued (Sec. 3097, Civ. C).

Lender's Name _____ Lender's Address _____

LICENSED CONTRACTORS DECLARATION: I hereby affirm under penalty of perjury that I am licensed under provisions of Chapter 9 (commencing with section 7000) of Division 3 of the Business and Professions Code and my license is in full force and effect.

License Class B License Number 517593 Date 5/13/04 Contractor Signature KJ Hazlett

OWNER-BUILDER DECLARATION: I hereby affirm under penalty of perjury that I am exempt from the contractors License Law for the following reason (Sec. 7031.5, Business and Professions Code; any city or county which requires a permit to construct, alter, improve, demolish, or repair any structure, prior to its issuance, also requires the applicant for such permit to file a signed statement that he or she is licensed pursuant to the provisions of the Contractors License Law (Chapter 9 (commencing with Section 7000) of Division 8 of the Business and Professions Code) or that he or she is exempt therefrom and the basis for the alleged exemption. Any violation of Section 7031.5 by any applicant for a permit subjects the applicant to a civil penalty of not more than five hundred dollars (\$500.00);

_____, I, as a owner of the property, or my employees with wages as their sole compensation, will do the work, and the structure is not intended or offered for sale (Sec. 7044, Business and Professional Code: The Contractors License Law does not apply to an owner of property who builds or improves thereon, and who does such work himself or herself or through his/her own employees, provided that such improvements are not intended or offered for sale. If, however, the building or improvement is sold within one year of completion, the owner-builder will have the burden of proving that he/she did not build or improve for the purpose of sale.)

_____, I, as owner of the property, am exclusively contracting with licensed contractors to construct the project (Sec. 7044, Business and Professions Code: The Contractors License Law does not apply to an owner of property who builds or improves thereon, and who contracts for such projects with a contractor(s) licensed pursuant to the Contractors License Law).

_____, I am exempt under Sec. _____ B & PC for this reason: _____
Date _____ Owner Signature _____

PAID
CITY OF SACRAMENTO
MAY 19 2004

IN ISSUING THIS BUILDING PERMIT, the applicant represents, and the city relies on the representation of the applicant, that the applicant verified all measurements and locations shown on the application or accompanying drawings and that the improvement to be constructed does not violate any law or private agreement relating to permissible or prohibited locations for such improvements. This building permit does not authorize any illegal location of any improvement or the violation of any private agreement relating to location of improvements.

I certify that I have read this application and state that all information is correct. I agree to comply with all city and county ordinances and state laws relating to building construction and hereby authorize representative(s) of this city to enter upon the abovementioned property for inspection purposes.

Date 5/13/04 Applicant/Agent Signature KJ Hazlett

WORKER'S COMPENSATION DECLARATION: I hereby affirm under penalty of perjury one of the following declarations:

_____, I have and will maintain a certificate of consent to self-insure for workers' compensation as provided for by Section 3700 of the Labor Code, for the performance of work for which the permit is issued.

_____, I have and will maintain workers' compensation insurance, as required by Section 3700 of the Labor Code, for the performance of the work for which this permit is issued. My workers' compensation insurance carrier and policy number are:

Carrier LIBERTY MUTUAL FIRE INS CO Policy Number WA269D004261012 Exp Date 08/01/2004



_____, (This section need not be completed if the permit is for \$100 or less) I certify that in the performance of the work for which this permit is issued, I shall not employ any person in any manner so as to become subject to the workers' compensation laws of California and agree that if I should become subject to the workers' compensation provisions of Section 3700 of the Labor Code, I shall forthwith comply with those provisions.

Date 5/13/04 Applicant Signature KJ Hazlett

WARNING: FAILURE TO SECURE WORKER'S COMPENSATION COVERAGE IS UNLAWFUL AND SHALL SUBJECT AN EMPLOYER TO CRIMINAL PENALTIES AND CIVIL FINES UP TO ONE HUNDRED THOUSAND DOLLARS (\$100,000) IN ADDITION TO THE COST OF COMPENSATION, DAMAGES AS PROVIDED FOR IN SECTION 3706 OF THE LABOR CODE, INTEREST AND ATTORNEY'S FEE.

THIS PERMIT SHALL EXPIRE BY LIMITATION IF WORK IS NOT COMMENCED WITHIN 180 DAYS.

THIS PLOT PLAN IS NOT FOR SALES PURPOSES. THIS PLOT PLAN IS FOR THE PURPOSES OF INDICATING COMPLIANCE WITH ZONING SETBACKS, GENERAL DRAINAGE DIRECTION, AND APPROXIMATE UTILITY CONNECTION. ALL OTHER DATA SHOWN HEREON IS CONCEPTIONAL. THIS PLOT PLAN DOES NOT REFLECT AS-BUILT CONDITIONS, RETAINING WALLS ARE OPTIONAL AND MAY OR MAY NOT BE CONSTRUCTED.

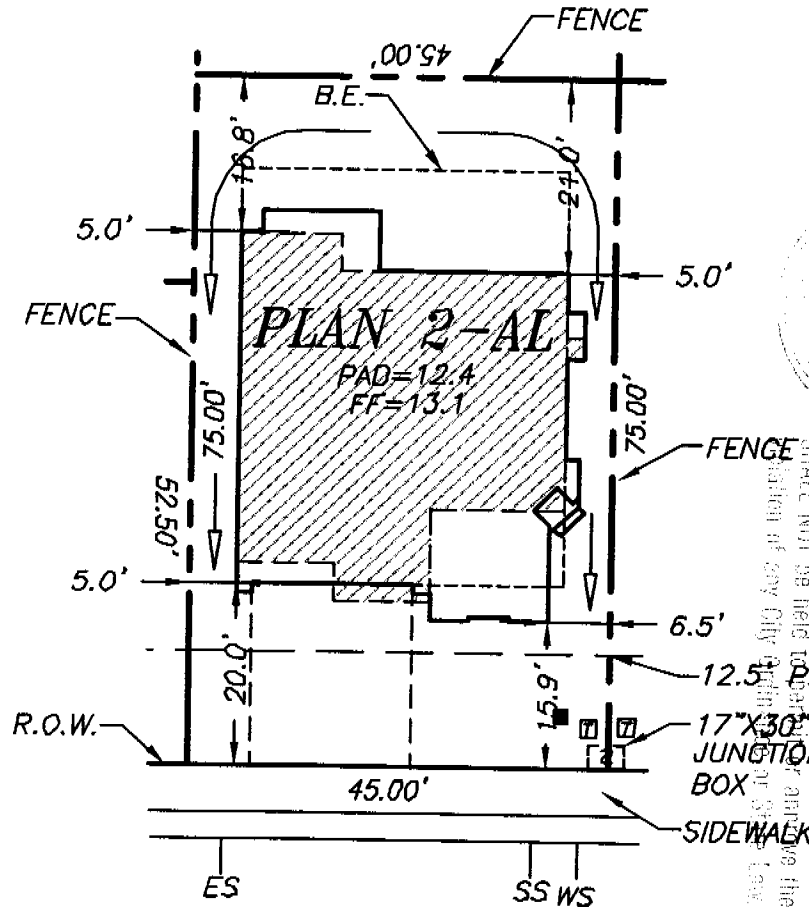

This set of plans and specifications must be kept on the job at all times and it is unlawful to make any changes or alterations from the same without written permission from the Building Inspection Division.
 The approval of this plan and specification shall not be held to indicate or approve the location of any City utility or other lines.

LEGEND

- ← DRAINAGE FLOW
- SS SEWER CONNECTION
- ☐ PHONE / CABLE PEDESTAL
- WS WATER SERVICE
- ▲ TRANSFORMER
- STREET LIGHT
- ☐ JUNCTION BOX
- FIRE HYDRANT
- ES ELECTRIC SERVICE
- 10"X12" VAULT




PULTE HOME CORPORATION
PARK LANE
AT REGENCY PARK
 CITY OF SACRAMENTO, CALIFORNIA

PLOT PLAN

1807 SPALETTA WAY

LOT AREA 3375 SQ.FT.



A.P.N.:

DATE: 4/7/04

SCALE: 1"=20'

UNIT: VILLAGE "B"

LOT NO.: 91

APPROVED:

2007-2008 Apr 24 10:14am

OMEGA PRODUCTS INTERNATIONAL, INC.

DIAMOND WALL INSULATING STUCCO SYSTEM

JOB ADDRESS:

ICBO Report #4004

1807 Spalletta Wy

Date of Job Completion 11/07/04

PLASTERING CONTRACTOR:

Name: Stellar ENTERPRISES

Address: 29054 Goetz RD

Telephone No: 909-244-0525

Contractor Number of Diamond Wall System _____

This is to certify that the exterior coating system on the building exterior at the above address has been installed in accordance with the evaluation report specified above and the manufacturer's instructions.

Date

JFK
Signature of authorized representative of
Plastering Contractor

This installation card must be presented to the building inspector after completion of work and before final inspection.



CAPITOL ENGINEERING LABORATORIES, INC.

631 Commerce Drive, Suite #200 • Roseville, California 95678 • (916) 786-2488

JOB REPORT

PAGE: 1

PROJECT NAME: PULTE Park LN

FILE NO. 5840

INSPECTOR: BARRY K... 7

DATE: 9/14/04

PERSONS CONTACTED: CUC

PERMIT #:

REFERENCE DOCUMENTS: ER 5779

WEATHER: Sunny

SERVICE PROVIDED: CONCRETE (INSP/SAMPLE ONLY/PU) MASONRY WELDING (SHOP/FIELD) SOILS

OTHER Epoxy Rebar

Worked the perimeter of epoxy Rebar @ Lot 71 on either side of Garage Door @ NW Corner #4's were spaced into exterior FIB @ ~ 8" OC. Spaced. Rebar Embedded ~ 8" into clean holes @ 25 locations base

Epoxy: Simpson Set 12 Exp 7/06

COMPLIANCE OF WORK: INSTALLED PER MFG DIRECTIONS

ATTACHMENTS:

EQUIPMENT/SUPPLIES USED:

NEXT VISIT:

REMARKS: PHPL-15

REVIEWED BY: B Barry K...

DATE: 9/14/04



CAPITOL ENGINEERING LABORATORIES, INC.

631 Commerce Drive, Suite #200 • Roseville, California 95678 • (916) 786-2488

JOB REPORT

PAGE: 1 of 1

FILE NO. 5840

DATE: 9-3-07

PERMIT #: P14P2-16

WEATHER: _____

PROJECT NAME: 7 mile Park Lane CVC

INSPECTOR: Sergio Aderso

PERSONS CONTACTED: Demando / Mark

REFERENCE DOCUMENTS: SRBA report # ER5279

SERVICE PROVIDED: CONCRETE (INSP/SAMPLE ONLY/PU) MASONRY WELDING (SHOP/FIELD) SOILS

OTHER

2 prof loaded 5/8" hold downs to 5875 lbs without any movement or failures as follows

- Lot 87 - 2 prof loaded (1) 5/8" HTT
- 88 - 2 prof loaded (4) 5/8" HTT
- 89 - 2 prof loaded (3) 5/8" HTT
- 90 - 2 prof loaded (3) 5/8" HTT
- 91 - 2 prof loaded (6) 5/8" HTT

COMPLIANCE OF WORK: Complies with ICB report # ER5279

ATTACHMENTS: _____

EQUIPMENT/SUPPLIES USED: Hydraulics

NEXT VISIT: _____

REMARKS: _____

REVIEWED BY: _____ DATE: _____



WALLACE • KUHL & ASSOCIATES INC.
 GEOTECHNICAL ENGINEERING • CONSTRUCTION TESTING

3050 Industrial Blvd.
 PO Box 1137
 West Sacramento
 California 95691
 916-372-1434

DATE 8-18-04		JOB NO. 4345.31		WEATHER Hot		TEMP. ° at ° at		AM PM		
PROJECT Park Lane Pulte					Technician I		Staff E/G			
LOCATION Lot 91					Technician II		Project E/G			
TYPE OF WORK P.T. Re-stress					Technician III		Senior E/G			
Inside 50 mi. radius <input checked="" type="checkbox"/>			Outside 50 mi. radius <input type="checkbox"/>			Nuclear Densities <input type="checkbox"/>		Principal E/G <input type="checkbox"/>		
PERSONNEL			REG. HRS	OT HRS	TOTAL HRS	TRAVEL	ON JOB	VEHICLE		MILES
David Crawford								71		

OBSERVATIONS:
 Observed re-stressing of 7/16" replacement cable running front to back. Cable has been re-stressed to 2.8 kips. Elongation 3 1/8".
 Calculated elongation = 3 1/8"

FIELD REPORT

Signed



WALLACE • KUHL & ASSOCIATES INC.
 GEOTECHNICAL ENGINEERING • CONSTRUCTION TESTING

3050 Industrial Blvd.
 PO Box 1137
 West Sacramento
 California 95691
 916-372-1434

DATE	8-3-04		JOB NO.	4345.31		WEATHER	Fair		TEMP.	* at	AM
PROJECT	Park Lane, Pulte Homes					Technician I	<input type="checkbox"/>	Staff E/G	<input type="checkbox"/>		
LOCATION	Lots 87-91, 9					Technician II	<input type="checkbox"/>	Project E/G	<input type="checkbox"/>		
TYPE OF WORK	P.T. Stressing OB.					Technician III	<input checked="" type="checkbox"/>	Senior E/G	<input type="checkbox"/>		
Inside 50 mi. radius	<input type="checkbox"/>	Outside 50 mi. radius	<input type="checkbox"/>		Nuclear Densities	<input type="checkbox"/>	Principal E/G	<input type="checkbox"/>			
PERSONNEL	REG. HRS	OT HRS	TOTAL HRS	TRAVEL	ON JOB	VEHICLE		MILES			
David Crawford	5					71		20			

OBSERVATIONS: Observed stressing of post tension cables in lots 87-91, 9. All cables have been stressed to 33 Kips and within tolerance of calculated elongations with the exception of the following:

Lot 91 - Second cable from S.W. corner running front to back broke. Need to fix.

Also stressed 5th cable from front of Lot 24 running side to side. 7/16" replacement cable stressed to 28 K and within tolerance.

FIELD REPORT

Signed



WALLACE • KUHL & ASSOCIATES INC.
 GEOTECHNICAL ENGINEERING • CONSTRUCTION TESTING

3050 Industrial Blvd.
 PO Box 1137
 West Sacramento
 California 95691
 916-372-1434

DATE 7-19-04	JOB NO. 4345.31	WEATHER	TEMP. * at * at	AM PM			
PROJECT Park Lane / Platte	Technician I <input type="checkbox"/>	Staff E/G <input type="checkbox"/>					
LOCATION Lots 9, 87-91	Technician II <input type="checkbox"/>	Project E/G <input type="checkbox"/>					
TYPE OF WORK Pit. Placement obs.	Technician III <input type="checkbox"/>	Senior E/G <input type="checkbox"/>					
Inside 50 mi. radius <input checked="" type="checkbox"/>	Outside 50 mi. radius <input type="checkbox"/>	Nuclear Densities <input type="checkbox"/>	Principal E/G <input type="checkbox"/>				
PERSONNEL	REG. HRS	OT HRS	TOTAL HRS	TRAVEL	ON JOB	VEHICLE	MILES
Wm Mandenhall						#36	30

OBSERVATIONS: Arrived on site at 10:30 am. Observed P.T. Tendon hardware and reinforcement placement in six lots #9, 91, located on Spaltonway lots 88, 89, 90 on Nickman way and Lot 87 on Hortonway. See findings below.

* Lot # 9 → Tendon chairs not in place @ South pop-out

* Lot # 91 → Live end anchor @ South-West corner not secured properly to forms.

* Lot # 90 → All P.T. tendons, hardware, and reinforcement found to be in place as per plans & details.

* Lot # 89 → Dead end anchor @ garage door not secured properly to forms.

* Lot # 88 → & Lot # 87 → All P.T. tendons hardware, reinforcement was found to be in place as per plans & details.

* → All deficiencies noted above have been corrected prior to my departure. No deficiencies to the best of my knowledge.

FIELD REPORT

Signed

Wm Mandenhall
