



1.4

Department of Utilities  
Engineering Services Division

CITY OF SACRAMENTO  
CALIFORNIA

**APPROVED**  
BY THE CITY COUNCIL

1395 35<sup>th</sup> Avenue  
Sacramento, CA 95822-2911  
phone (916) 264-1400  
fax (916) 264-1497/1498

**OCT 27 1998**

OFFICE OF THE  
CITY CLERK

October 8, 1998

City Council  
Sacramento, California

Honorable Members in Session:

**SUBJECT: SUMP 35 PUMP STATION (PN: WG56) - APPROVAL OF CONTRACT CHANGE ORDER 4 AND RESTORATION OF CITY MANAGER AUTHORITY**

**LOCATION AND COUNCIL DISTRICT:**

Sump 35 Pump Station Project is in Council District 4 near Alma Vista and Pocket Road. See location map.

**RECOMMENDATION:**

Staff recommends that the City Council:

- Approve Change Order 4 with EAI International (contract #98-016) for \$95,913.51 and;
- Restore the City Manager's authority to issue change orders on this contract.

**CONTACT PERSON:** Andrew A. Hunt, Senior Engineer, 433-6620  
Gary Reents, Engineering Services Division Manager, 433-6633

**FOR COUNCIL MEETING OF:** October 27, 1998

**SUMMARY**

Per City Council direction, the Sump 35 Pump Station Project was informally rebid on December 17, 1997. Bids were received from the three (3) invited contractors and opened by the Project Manager on January 14, 1998. The low bidder was EAI International with a bid of \$453,848. Work is currently underway. Change Order 4 is required for the project to function as intended.



CITY OF SACRAMENTO  
DEPARTMENT  
OF UTILITIES

*Making a Difference in Your Neighborhood*

City Council  
October 27, 1998  
Sump 35 Pump Station (PN: WG56)

## **COMMITTEE/COMMISSION ACTION**

None.

## **BACKGROUND INFORMATION**

- The pump station is located at the end of Myrtle Vista Avenue near Pocket Road and Interstate 5; piping starts from Sharon Way and extends to Pump Station 35.
- Approximately 450 feet of pipe will be removed and replaced with approximately 1,120 feet of 30-36 inch drainage main. This includes placing approximately six manholes, 270 feet of drain lead, 12 ditch boxes and one storm sump.

The following are explanations of the change order items:

1. Time and materials costs for repairs on the 30" and 36" HDPE storm drain pipes totaled \$91,836. The responsibility for these costs will be split three ways between the City of Sacramento, EAI International and ADS Pipe. The City is fronting 2/3 of the costs and will seek reimbursement from ADS Pipe. The cost total for this item is \$61,224.01
2. The City agreed to pay extra handling cost to bring in large amounts of aggregate base for backfill due to the unsuitability of the native soil for backfill. The total cost for this item is \$31,189.50
3. The City agreed to pay for one additional well point because of claimed excessive pumping demands. The total cost for this item is \$4,500.

The change order is attached as Exhibit 1.

## **ENVIRONMENTAL DETERMINATION**

This project is categorically exempt pursuant to Section Number 15301 (b) and 15302 (c) of the California Environmental Quality Act.

City Council  
October 27, 1998  
Sump 35 Pump Station (PN: WG56)

**FINANCIAL CONSIDERATIONS**

The total budget for the project (PN:WG56) is \$800,000. As of October 8, 1998, there is \$49,500 remaining in the project. The City will be processing a future change order that will decrease the amount of work done on contract which should cover the difference between the total change order cost and the available funds in the project.


**POLICY CONSIDERATIONS**

This action is consistent with Chapter 58, Article IV, Section 58.602 of the City Code concerning change orders.

**MBE/WBE**


This project included MBE/WBE participation goals of 10.57% MBE and 9.5% WBE as required by Resolution No. 93-619, relating to MBE/WBE participation goals and policies adopted by the City Council on November 2, 1993. EAI International obtained participation of 0.33% and 5.71%, respectively, which are short of the goals but a Good Faith Effort was documented.

Respectfully submitted,




*FOR* Gary A. Reents  
Engineering Services Manager

RECOMMENDATION APPROVED:




WILLIAM H. EDGAR  
City Manager


APPROVED:



JAMES G. SEQUEIRA  
Director of Utilities

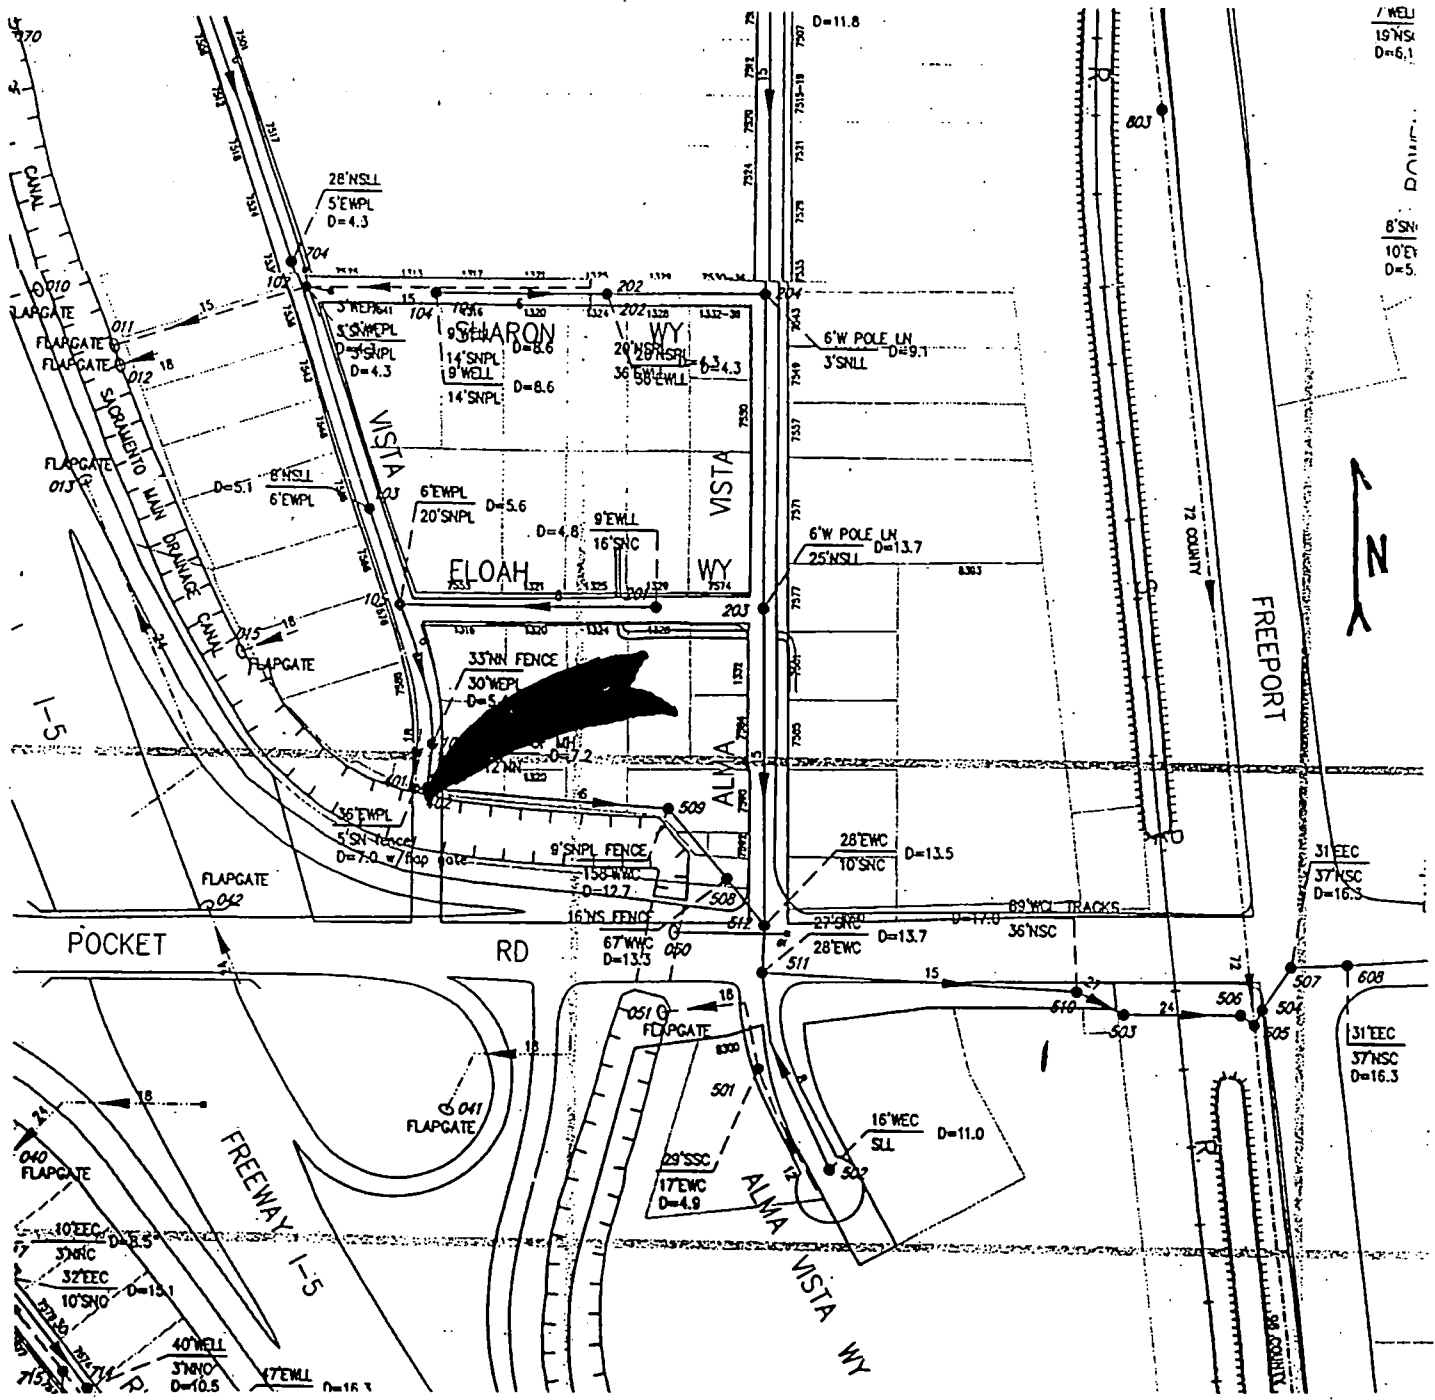

**LOCATION MAP**  
NO SCALE

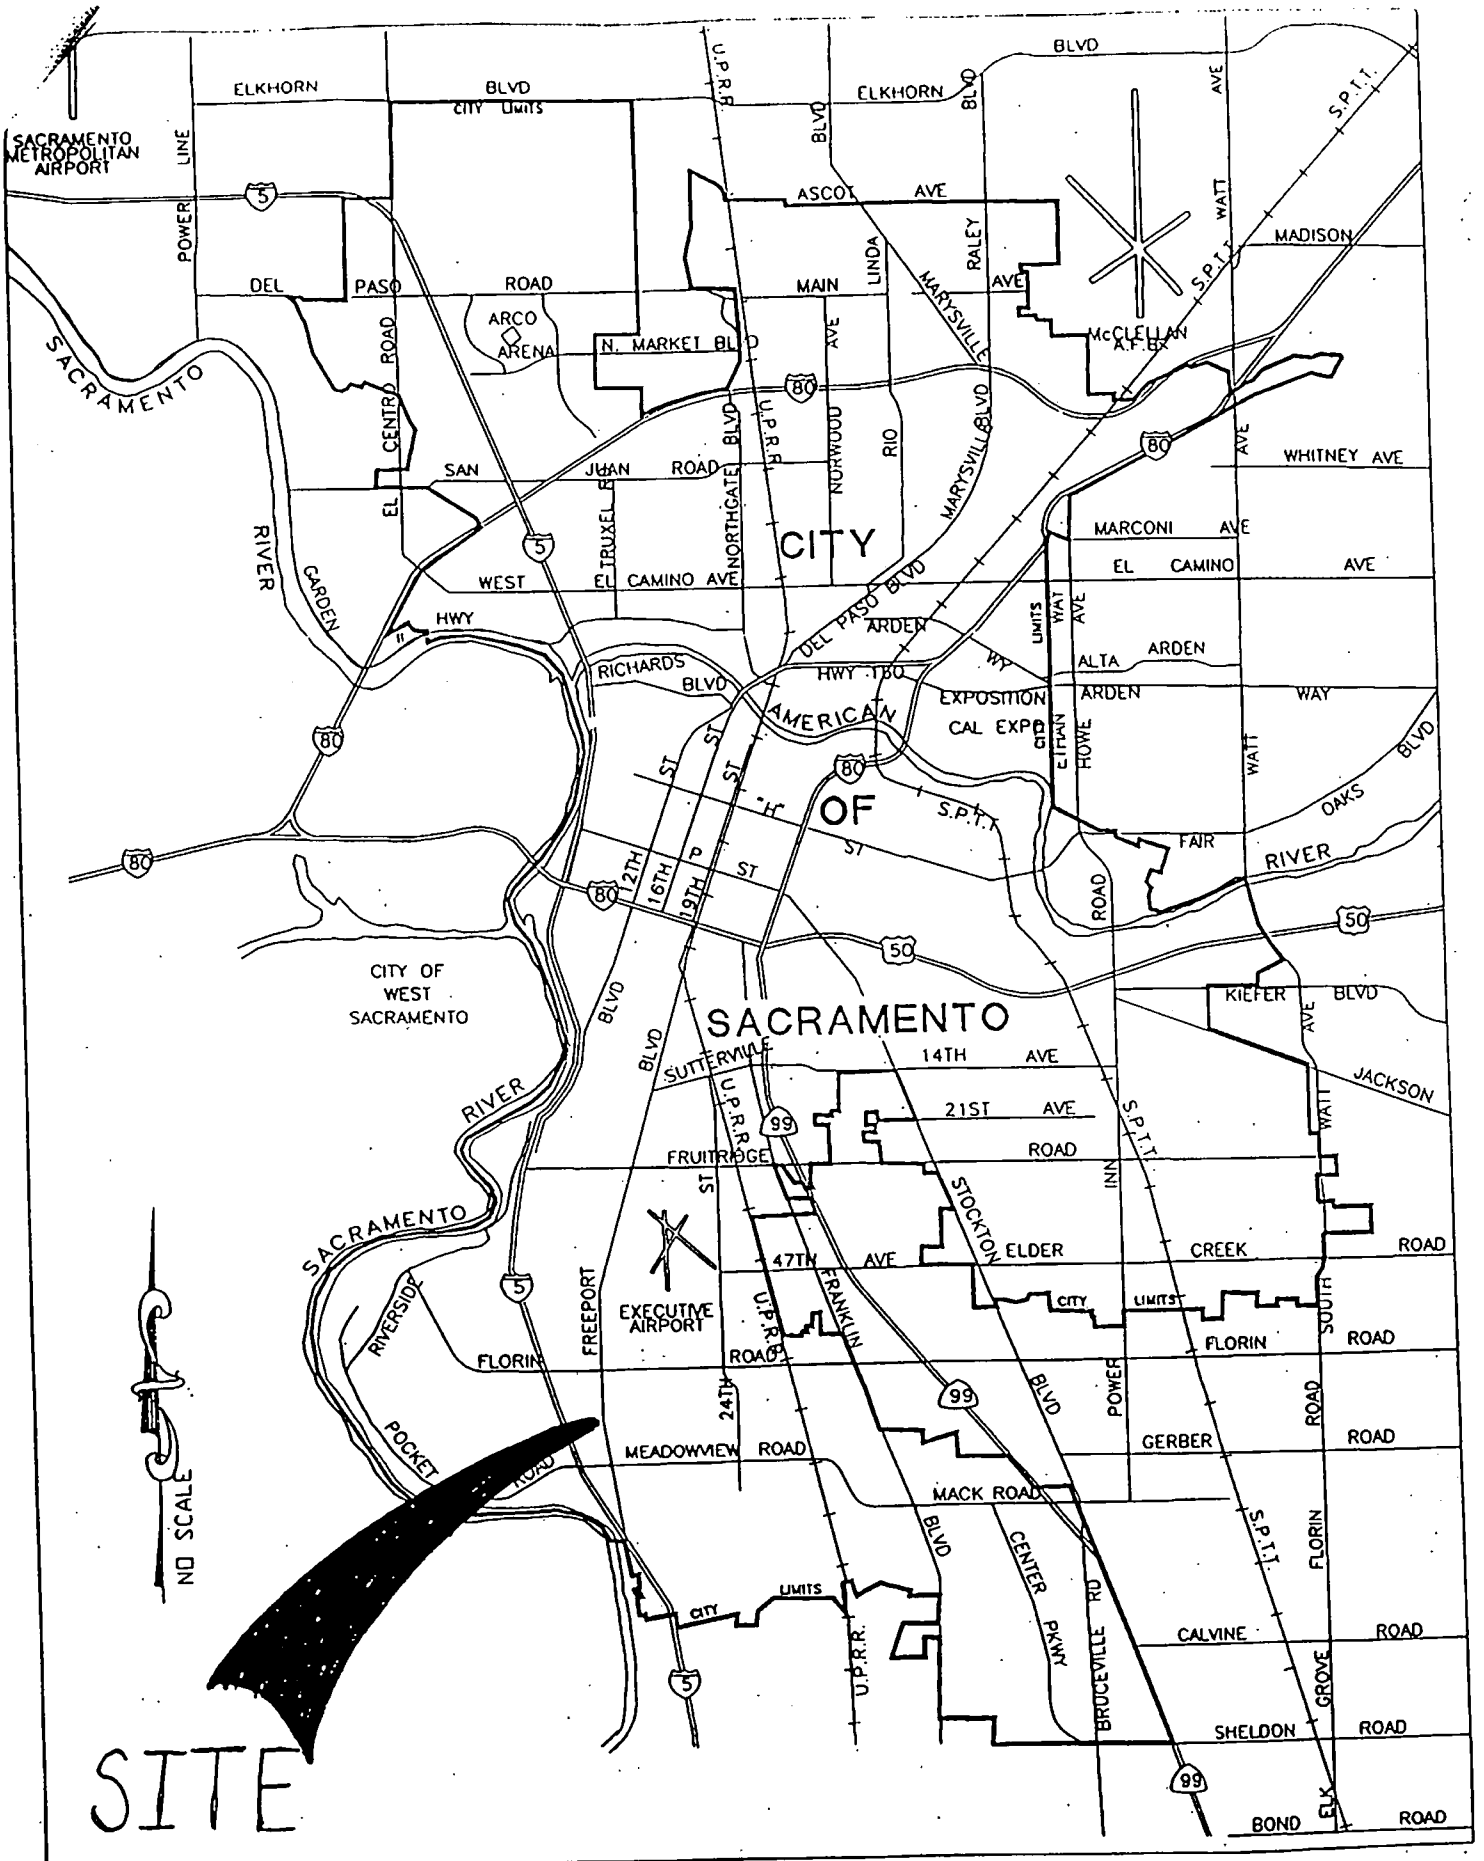

SITE

VICINITY MAP

APPROVED  
BY THE CITY COUNCIL

RESOLUTION NO. 98-533

OCT 27 1998

ADOPTED BY THE SACRAMENTO CITY COUNCIL

OFFICE OF THE  
CITY CLERK

ON DATE OF \_\_\_\_\_

RESOLUTION APPROVING CONTRACT CHANGE ORDER 4 AND RESTORATION OF CITY MANAGER AUTHORITY FOR THE SUMP 35 PUMP STATION PROJECT (PN: WG56)

BE IT RESOLVED BY THE SACRAMENTO CITY COUNCIL THAT:

1. The City Manager and City Clerk are authorized to sign and execute Contract Change Order 4 with EAI International, for \$95,913.51 for the Sump 35 Pump Station Project (PN:WG56).
2. The City Manager's authority to issue change orders on this contract is restored.

\_\_\_\_\_  
MAYOR

ATTEST:

\_\_\_\_\_  
CITY CLERK

\_\_\_\_\_  
FOR CITY CLERK USE ONLY

RESOLUTION NO. \_\_\_\_\_

DATE ADOPTED: \_\_\_\_\_

4
